

Harlandale Independent School District

UHS-HISD Clinic Renovation at Collier Learning Center




Building Committee Meeting
February 8, 2016

UHS-HISD Clinic Renovation at Collier Learning Center

Renovated Clinic includes:

- Waiting Room / Reception
 - 4 Exam Rooms
 - Manager's Office
 - Staff Work and Break Rooms
 - Lab, Storage and Support Areas
-

UHS-HISD Clinic Renovation at Collier Learning Center

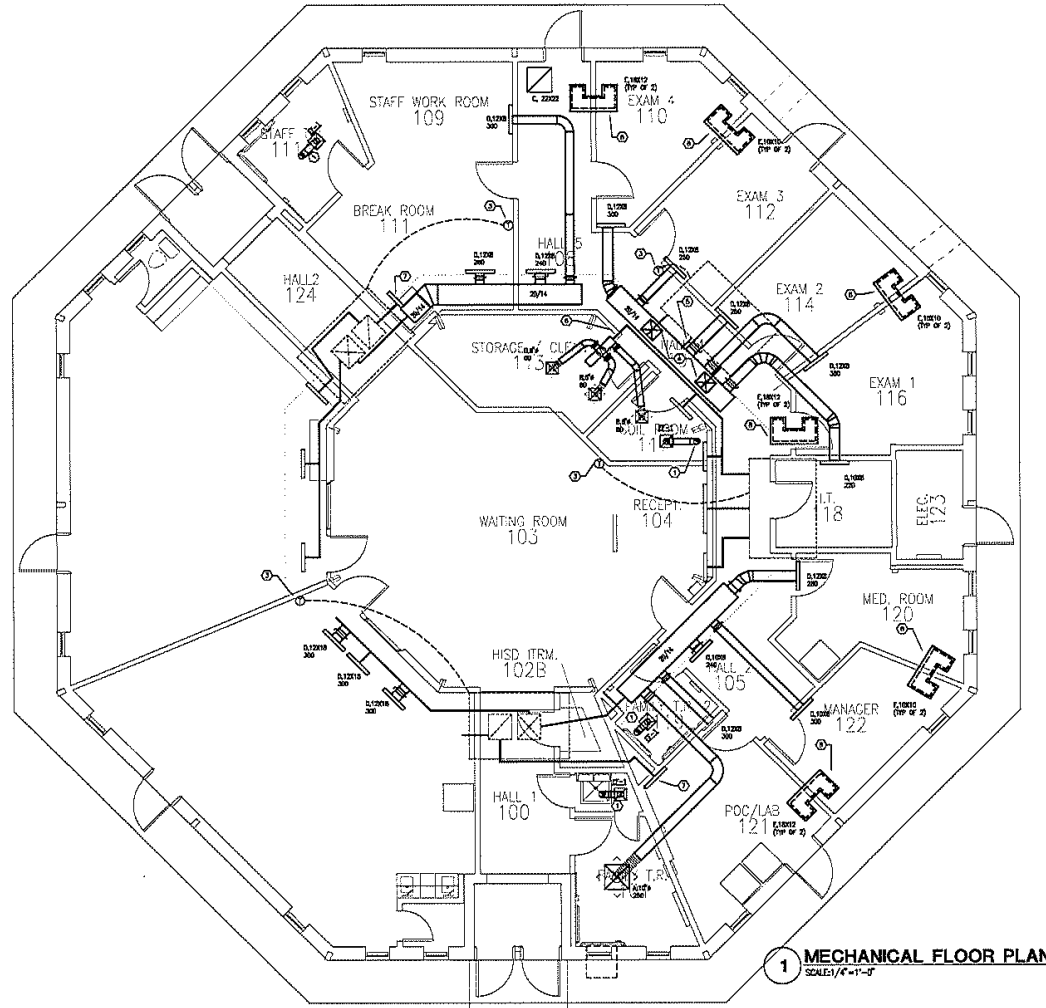

UHS-HISD Clinic Renovation at Collier Learning Center

Original Budget:	\$386,000
<u>Approved Proposal:</u>	<u>\$367,800</u>

Under Budget:	\$18,200
<u>Additional Savings:</u>	<u>\$2,100</u>
Total Savings:	\$20,300

UHS-HISD Clinic Renovation at Collier Learning Center

Current Status:

- Substantial Completion Date: October 12, 2015
- *Actual* Substantial Completion Date: August 26, 2015
- Project 100% Complete
- No Change Orders charged to HISD
- Facility turned over to UHS Clinic Staff for daily operation.

**Project Completed Ahead
of Schedule**
